

Tillsonburg Community Centre – Construction Update

February 2024

Construction progress continues for the south addition to the Tillsonburg Community Centre.

The month of February saw further structural steel and metal roof deck erection at the second floor to roof framing levels and most notably the start of the exterior wall and parapet installation.

Internally, interior block work, HVAC, plumbing and electrical has progressed within the new accessible change room area. HVAC reconfiguration has also commenced within the second floor level and coordination for new fire protection has begun.


As work continues into March, further progress with the exterior wall construction and interior areas of the accessible change room and main lobby should be observed.




Exterior: View towards the north (South Entry from Hardy Ave.)



Interior: View towards the main entry and lobby area

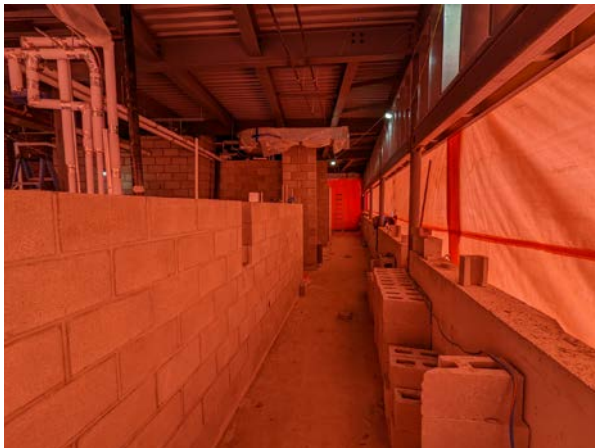

Interior: View towards the east within the new accessible change room area

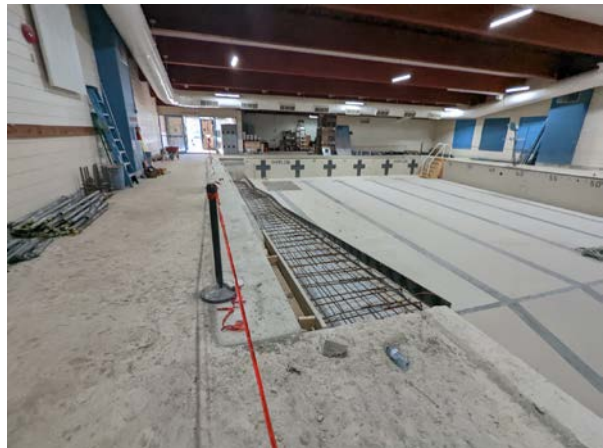

Interior: View towards the west within Kinsmen Pool

Anticipated work for March 2024:

- Structural steel and masonry work will continue and near completion
- HVAC, plumbing, electrical rough-ins will continue
- Sprinkler piping installation will commence
- Exterior wall assembly construction will continue
- Roof parapet and curb construction will continue
- Roofing assembly installation will commence
- Pouring of the second floor level will commence

a+LiNK Architecture Inc. will continue to provide monthly construction updates on the Tillsonburg Community Centre Addition.
